




ONAP Release Planning

Gildas Lanilis – ONAP Release Manager

Sept 27, 2018

ONAP Dublin Release Calendar Proposal

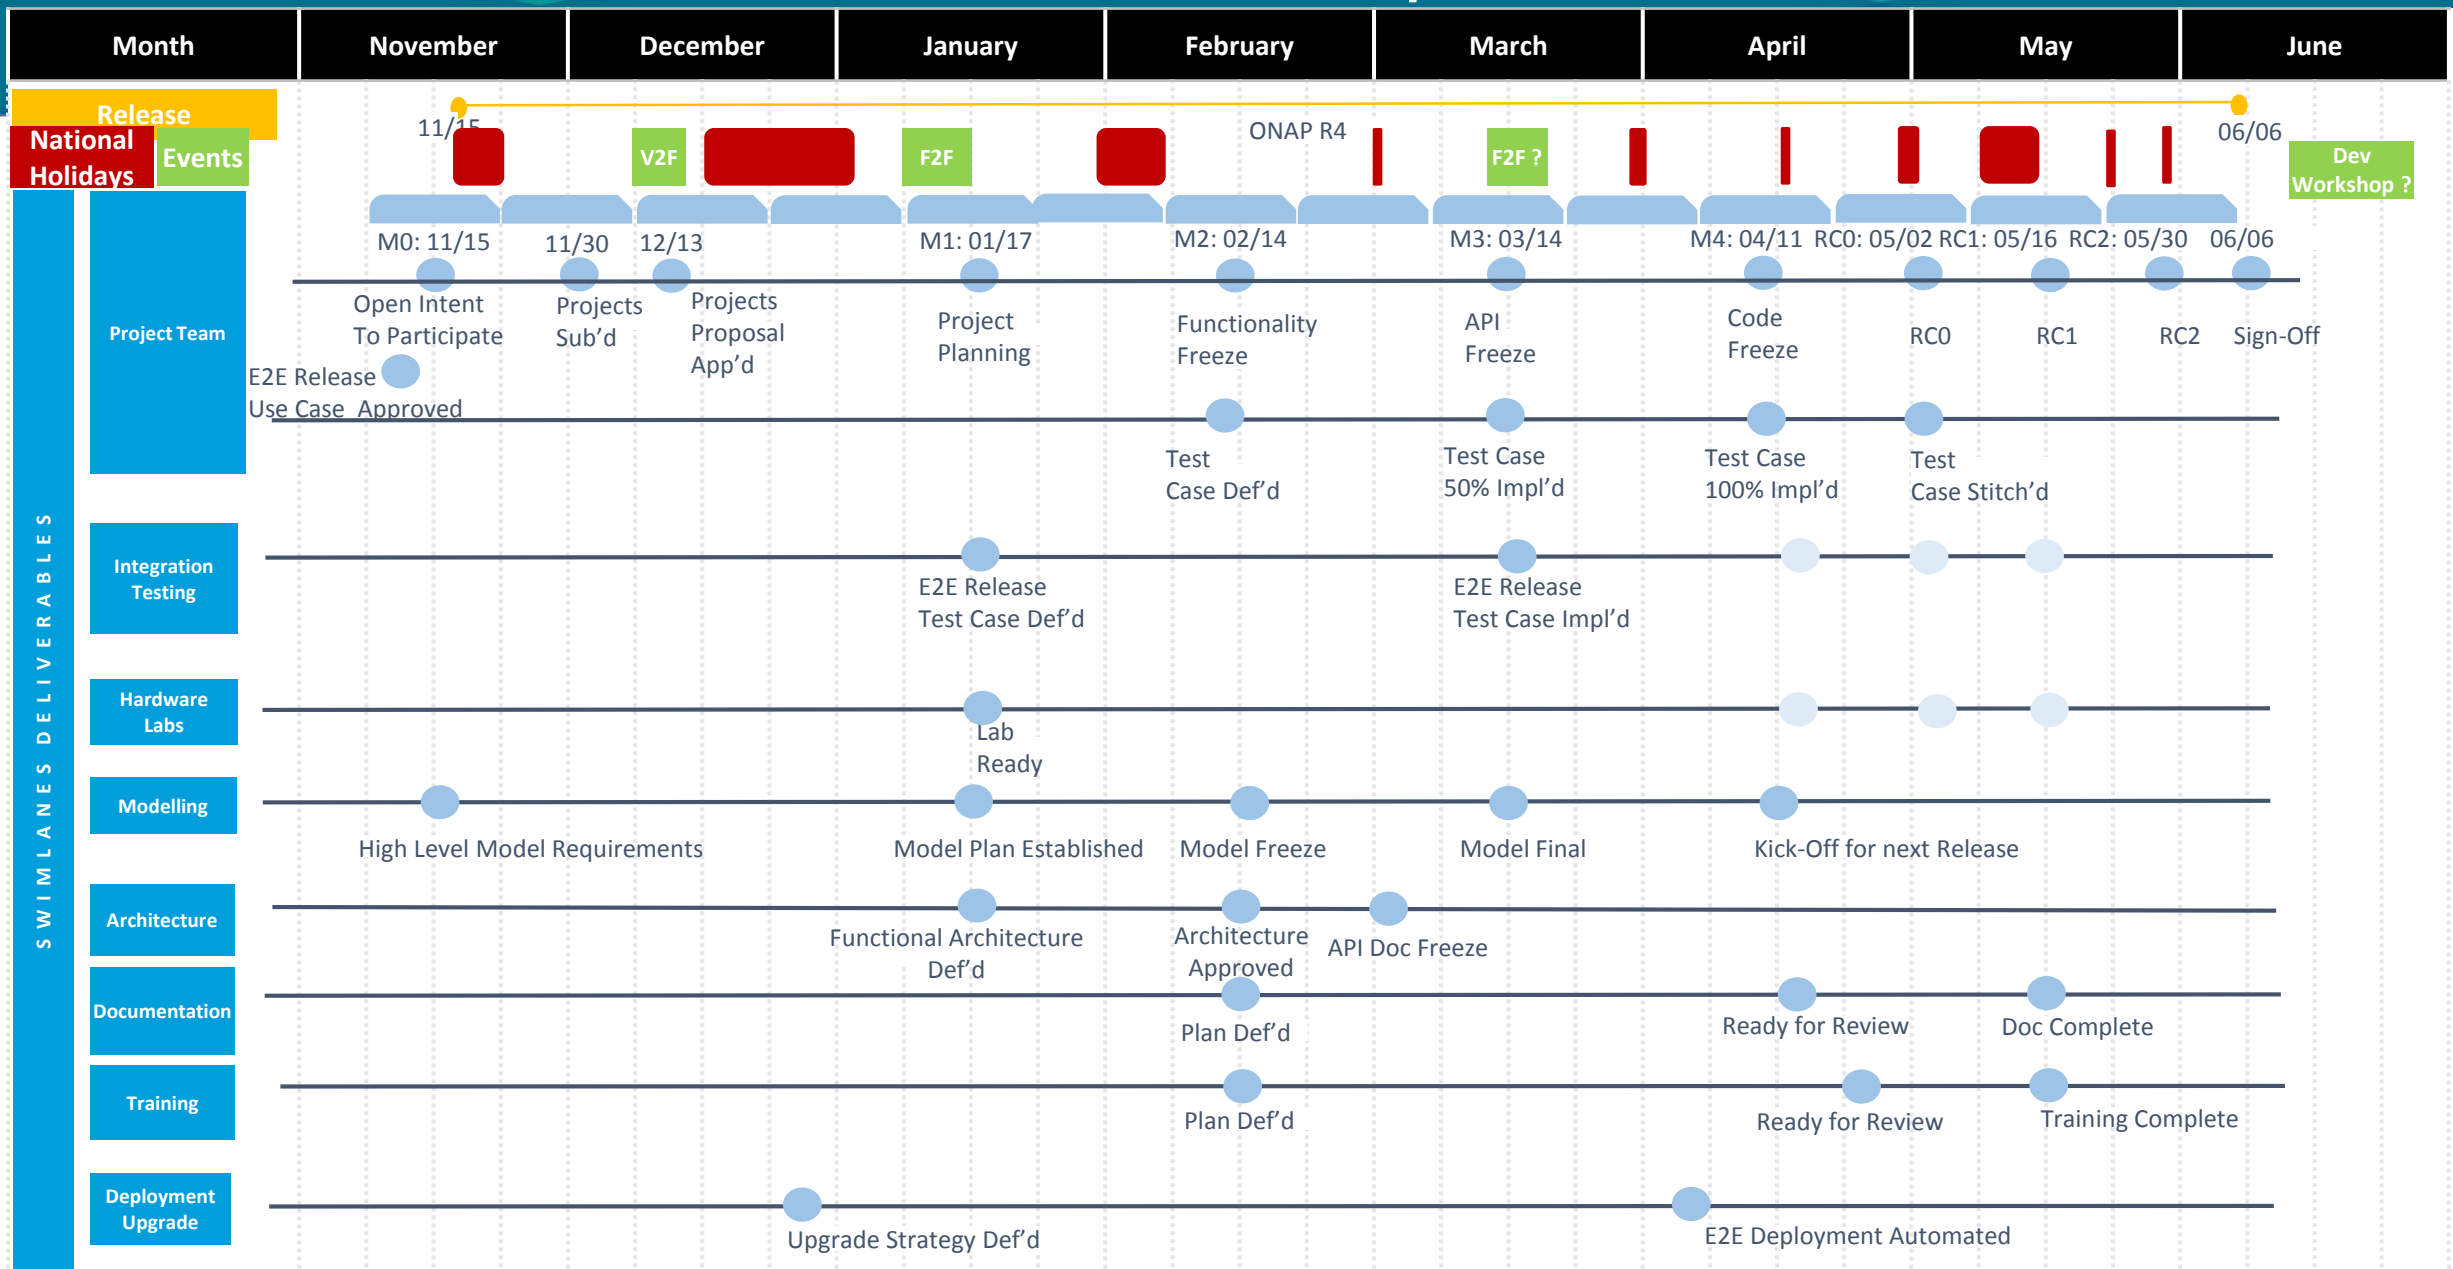

Dublin Timeline

| | ONAP Dublin | Milestone Duration (weeks) |
|--------------------------------------|----------------|----------------------------------|
| M0: Release Kick-Off | 15-Nov | 9 |
| Pre-M1 Availability of project scope | 7-Jan | |
| M1: Release Planning | 17-Jan | 4 |
| M2: Functionality Freeze | 14-Feb | 4 |
| M3: API Review | 14-Mar | 4 |
| M4: Code Freeze | 11-Apr | 3 |
| RC0 | 2-May | 2 |
| RC1 | 16-May | 2 |
| RC2 | 30-May | 1 |
| Sign-Off | 6-Jun | |
| Release Duration | | 29 |

Former Releases timeline

| | ONAP Amsterdam | Milestone Duration (weeks) | | Revised Amsterdam ONAP Planning | Revised Milestone Duration (weeks) |
|--------------------------|-------------------|----------------------------------|--------------------------|------------------------------------------|---------------------------------------------|
| M0: Release Kick-Off | 4-May | 8 | M0: Release Kick-Off | 4-May | 8 |
| M1: Release Planning | 29-Jun | 5 | M1: Release Planning | 29-Jun | 5 |
| M2: Functionality Freeze | 3-Aug | 3 | M2: Functionality Freeze | 3-Aug | 3 |
| M3: API Review | 24-Aug | 3 | M3: API Review | 24-Aug | 5 |
| M4: Code Freeze | 14-Sep | 2 | M4: Code Freeze | 28-Sep | 2 |
| RC0 | 28-Sep | 2 | RC0 | 12-Oct | 2 |
| RC1 | 12-Oct | 2 | RC1 | 26-Oct | 2 |
| RC2 | 26-Oct | 1 | RC2 | 9-Nov | 1 |
| Sign-Off | 2-Nov | | Sign-Off | 16-Nov | |
| Release Duration | | 26 | Release Duration | | 28 |

| | ONAP Casablanca | Milestone Duration (weeks) |
|--------------------------------------|--------------------|----------------------------------|
| M0: Release Kick-Off | 24-May | 5 |
| Pre-M1 Availability of project scope | 21-Jun | |
| M1: Release Planning | 28-Jun | 4 |
| M2: Functionality Freeze | 26-Jul | 4 |
| M3: API Review | 23-Aug | 4 |
| M4: Code Freeze | 20-Sep | 3 |
| RC0 | 11-Oct | 2 |
| RC1 | 25-Oct | 2 |
| RC2 | 8-Nov | 1 |
| Sign-Off | 15-Nov | |
| Release Duration | | 25 |

| | ONAP Beijing | Milestone Duration (weeks) | Revised ONAP Beijing | Revised Milestone Duration (weeks) |
|--------------------------------------|-----------------|----------------------------------|-------------------------|---------------------------------------------|
| M0: Release Kick-Off | 16-Nov | 9 | 16-Nov | 9 |
| Pre-M1 Availability of project scope | 8-Jan | | 8-Jan | |
| M1: Release Planning | 18-Jan | 4 | 18-Jan | 4 |
| M2: Functionality Freeze | 15-Feb | 3 | 15-Feb | 3 |
| M3: API Review | 8-Mar | 3 | 8-Mar | 3 |
| M4: Code Freeze | 29-Mar | 3 | 29-Mar | 3 |
| RC0 | 19-Apr | 2 | 19-Apr | 2 |
| RC1 | 3-May | 2 | 3-May | 2 |
| RC2 | 17-May | 1 | 17-May | 3 |
| Sign-Off | 24-May | | 7-Jun | |
| Release Duration | | 27 | | 29 |



ONAP

OPEN NETWORK AUTOMATION PLATFORM

谢谢
